BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	: Executive Engineer Byatarayanapura Division
Project Name	: Package2, includes 5 works of Rs.245.00 lakhs 1)Improvements to Roads and Drains at Mariyannapalya Church to Defence Layout and Dynasty Layout in Ward No:06 Byatarayanapura Sub Division. 2)Improvements to Drains and Asphalting to Roads at Balaji layout Near Railway Gate in Ward No:06 Byatarayanapura Sub Division. 3)Improvements to Drains and Asphalting to Roads at Vidyanagara Layout and Surrounding area in Ward No: 06 Byatarayanapura Sub Division. 4)Improvements to Drains and Asphalting to Roads at Bharathnagara new mill Road in Ward No: 06 Byatarayanapura Sub Division. 5) Improvements to Drains and Asphalting to Roads at Shiradi Sai Nagar and Hegadenagar in Ward No:06 Byatarayanapura Sub Division.
Consultants	: Rudraprasad Consultants
Project Manager /Team Leader	: Karthik Reehan
Project Start Date	: 25-Jun-18
Project End Date	: 25-Oct-18
Project Length in Months	: 4 months

Sl. No	Assignment	Unit	Boq Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Earthwork excavation by manual means in ordinary soil	Cum	3418.65	3228.01	94	27-06-18	11-10-19	471
2	Providing granite slabs of selected quality roughly dressed having a size of 7.5cms thick and fixed in cement mortar (1:6)	Sqm	3245.10	3244.38	100	10-07-18	11-10-19	458
3	Excavation for roadwork in soil with hydraulic excavator of 0.90 cum bucket capacity	Cum	3005.10	1848.49	62	17-07-18	11-10-19	451
4	Providing,laying, spreading and compacting wet mix macadam	Cum	1972.34	1619.78	82	23-07-18	11-10-19	445
5	Providing and applying primer coat with SS bitumen emulsion on prepared surface of granular Base such as WBM WMM including clearing of road surface	Sqm	8575.40	5274.27	62	30-07-18	11-10-19	438
6	Cleaning the existing black topped surface.	Sqm	22028.10	19156.10	87	03-08-18	11-10-19	434
7	Providing and applying tack coat using 80/100 grade bitumen (VG10) on prepared black topped surfaces	Sqm	26289.10	19156.10	73	07-08-18	11-10-19	430
8	Providing and laying bituminous concrete 40 mm	Cum	1051.56	766.24	73	07-08-18	11-10-19	430
9	Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface	Sqm	948.80	308.12	32	01-09-18	11-10-19	405
11	Providing and removing centering, shuttering, strutting, propping etc., for columns, pillars, post and structs, square/rectangular/polygon in plan	Sqm	2014.10	2014.10	100	07-08-18	11-10-19	405
12	Providing and laying in position reinforced cement concrete of design mix M20	Cum	270.95	114.36	42	07-08-18	11-10-19	405
13	Providing T.M.T steel reinforcement for R.C.C work	tonne	16.11	270.93	1682	07-08-18	11-10-19	430
14	Providing and laying in position plain cement concrete of mix 1:3:6	Cum	332.59	2129.10	640	07-08-18	11-10-19	405
15	Construction of un-reinforced plain cement concrete pavement,thickness as per design, over a prepared sub base	Cum	139.38	1143.55	820	07-08-18	11-10-19	405
16	Vaccum de-watering with vaccum pump and suction mat and compaction with skin floater	Sqm	1393.80	994.38	71	07-08-18	11-10-19	405
E1	Construction of embankment with approved material Gravel/Murrum with all lifts and leads,	Cum	995.10	994.38	100	07-08-18	11-10-19	405

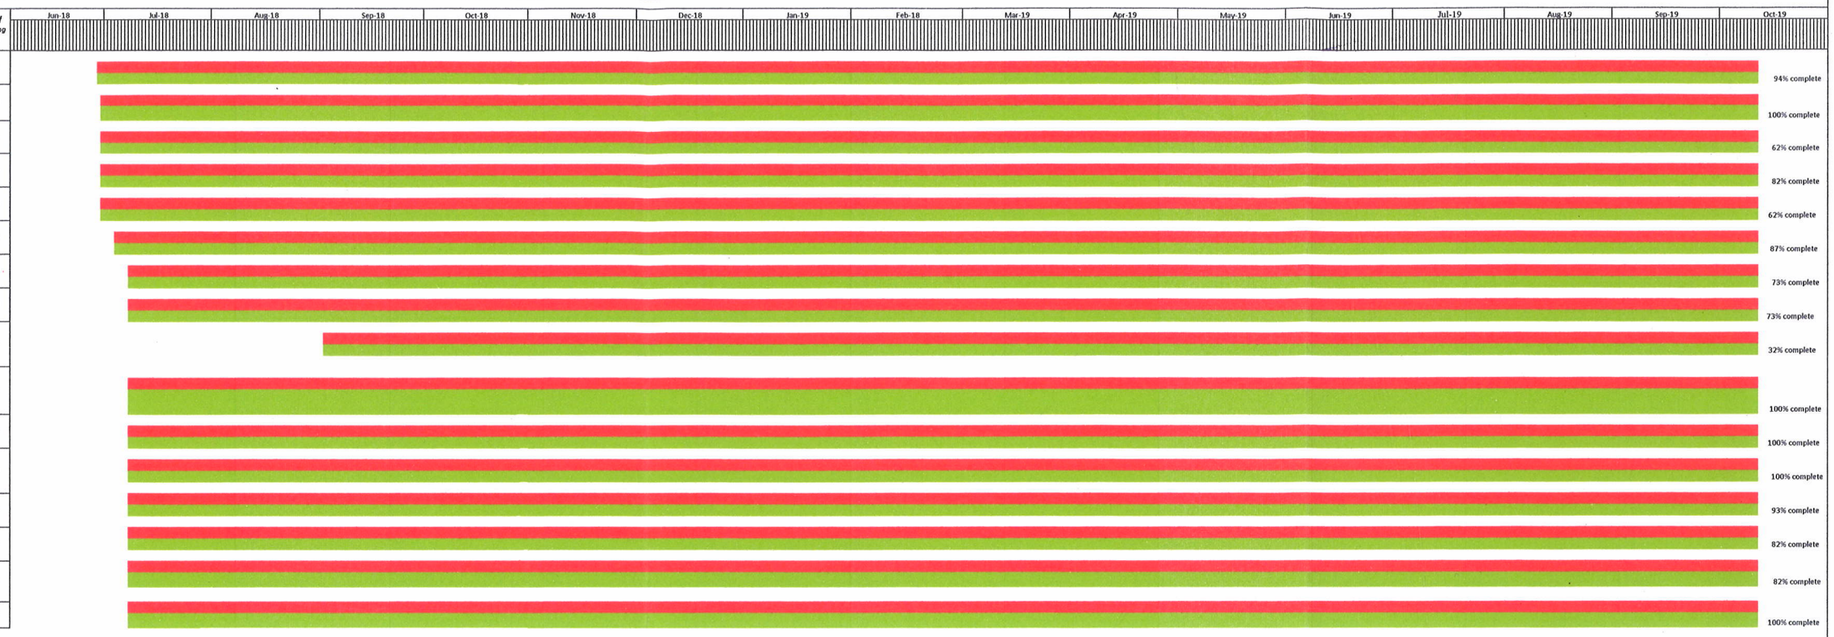

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬ.ಬ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

ಅಂಚೆಯ
ಮುದ ಉಪ ವಿಭಾ

RUDRAPRASAD CONSULTANTS
BANGALORE
